# West Windsor- Plainsboro

Regional School District

# Referendum Services FVHD #5063

#### Referendum Project Update

**September 17, 2019** 





# Fire Alarm System Replacement Project

- Maurice Hawk ES and Town Center ES are completed!!
- Village ES work will commence in October with completion by end of year.
- Dutch Neck ES and Millstone River ES to follow- completion Spring/Summer 2020.
- Community MS, HS South and Wicoff ES new systems will be coordinated with construction projects.






### **Emergency Generator Project**

- Work underway at all sites (Thomas Grover MS, Community MS, Village ES, Millstone River ES)
- Generators have been ordered and delivery is expected in November.
- Completion of project by end of 2019.
- HS South generator will be installed with new construction project.









# Thomas Grover Middle School-Schedule Ready to Start!!

| Event                                 | Date                   |
|---------------------------------------|------------------------|
| Advertise for Bids                    | October 1, 2019        |
| Open Bids/Award Project               | November 19, 2019      |
| Start Construction- Weather Dependent | On/about March 2, 2020 |
| Complete Construction                 | June 25, 2021          |





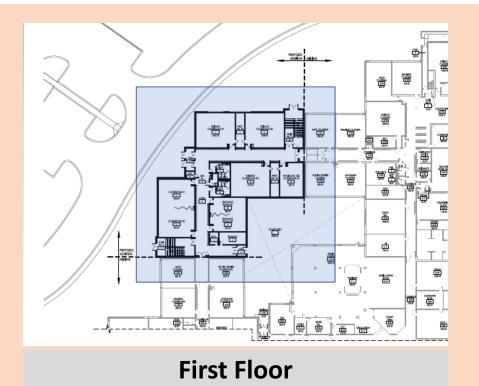

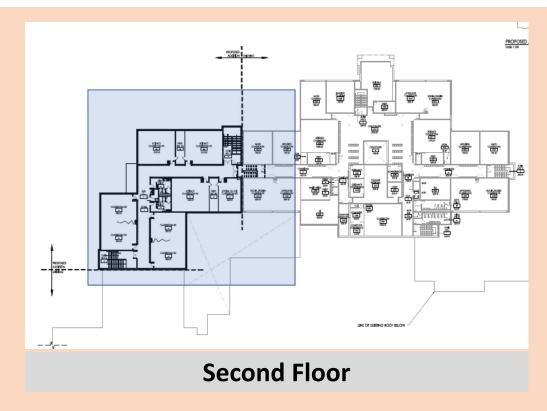



#### Thomas Grover MS- Floor Plan







# Community Middle SchoolOverall Schedule

| Event                                 | Date                   |
|---------------------------------------|------------------------|
| Advertise for Bids                    | November 4, 2019       |
| Open Bids/Award Project               | December 17, 2019      |
| Start Construction- Weather Dependent | On/about March 2, 2020 |
| Complete Construction                 | December 2022          |







#### **Community Middle School- Project Phasing**

| Event  | Date                              |
|--|-----------------------------------|
| Start Construction- Weather Dependent  | On about March 2, 2020            |
| Complete New Additions   | August 14, 2021                   |
| Renovations <u>Phase 1A</u> - Girls Locker Room, Main Office   | June 22, 2021 – August 28, 2021   |
| Renovations <u>Phase 1B</u> (Pending New Addition)-<br>Gym, Music Areas, Science                     | June 22, 2021 – July 29, 2022     |
| Renovations Phase 2A - Kitchen   | June 27, 2022 – August 26, 2022   |
| Renovations <a href="Phase 28">Phase 28</a> - Art/General Music, Technology Classroom and Auditorium | June 27, 2022 – December 30, 2022 |
| Complete All Construction  | December 30, 2022                 |






#### **Community MS- Site Improvements**

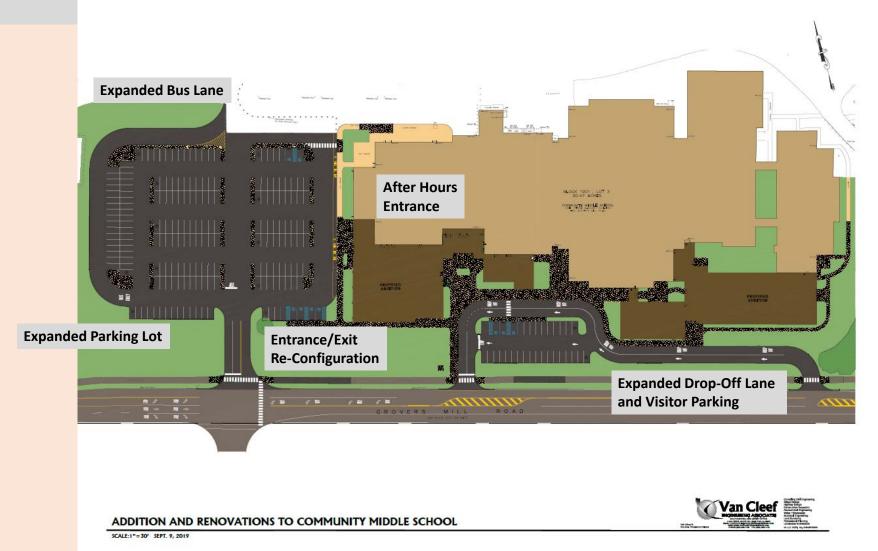





# Community MS- Athletic Fields

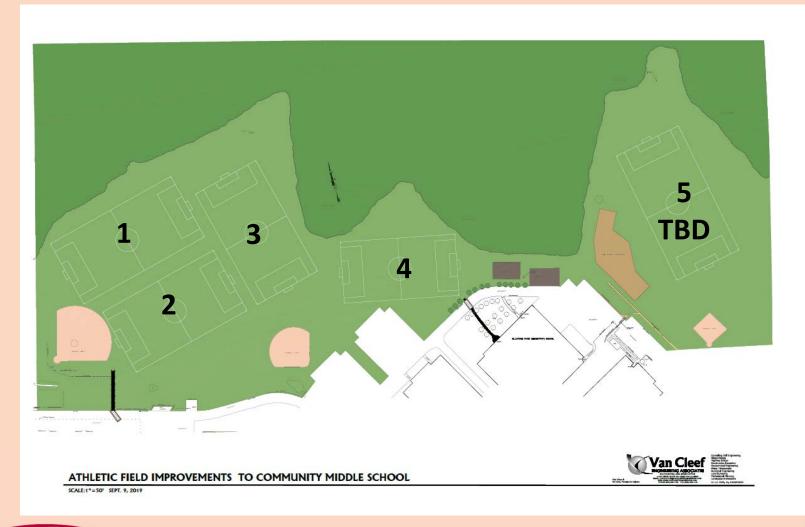



# Community Middle School

#### First Floor Work Areas by Function









# **Community Middle School**

#### Second Floor Work Areas by Function

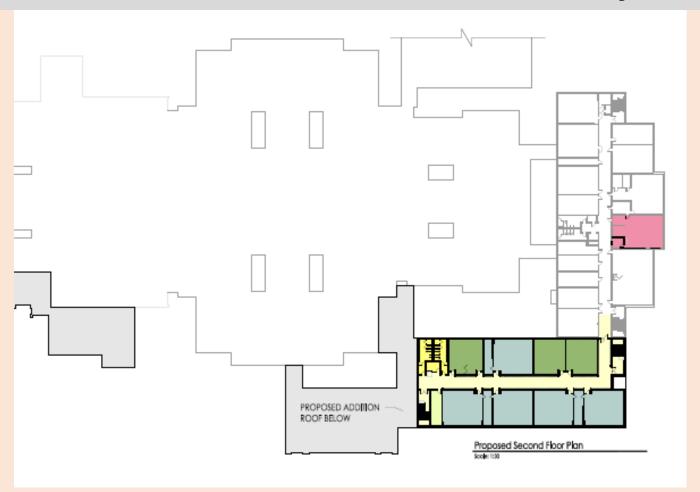







# Other Referendum Projects- Construction

Additions/Renovations to HS South

Bid March 2020 Complete Dec 2021

Additions/Renovations to HS North

Bid Fall 2020 Complete Aug 2021

Additions/Renovations and HVAC Improvements to Wicoff ES

Bid Fall 2020

Complete Aug 2021





# Other Referendum Projects

Misc Renovations (Toilet Rooms, Secure Vestibules, Etc.)

Bid January 2020 **Complete Aug 2020** 

Media Center Renovations at All Elementary Schools

Bid Group 1 January 2020 **Complete Aug 2020** 

Bid Group 2 January 2021 Complete Aug 2021





# Other Referendum Projects

**HVAC Improvements** at HS North, Millstone River

Bid Fall 2019

Complete August 2021

| Event                       | Date                        |
|-----------------------------|-----------------------------|
| Advertise for Bids on/about | October 1, 2019             |
| Open Bids/Award Project     | November 19, 2019           |
| Chiller Replacement         | On/about March 2, 2020      |
| Boiler Replacement          | March 2020 – September 2020 |
| Phase 1 Classroom Areas     | Summer 2020                 |
| Phase 2 All Other Areas     | Summer 2021                 |





#### Under Construction- Maurice Hawk School

Renovation areas
 completed and re occupied for new school
 year.

 New addition is behind schedule but progressing.
 Anticipated completion by mid- November.









#### **Town Center School- Under Construction**

- Renovation areas completed and reoccupied for new school year.
- Work on new addition is progressing well.
- Anticipated completion prior to end of November.









#### Referendum Project Status Report

# Thank You!!





